


004 Tentativ fremdriftsplan

ID	Task Mode	Task Name	Duration	Start	Finish	Timeline											
						May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr
1		Løvstakkveien - Kommunale boliger	330 days	Mon 23.01.23	Fri 31.05.24	[Summary bar]											
2		Rammetillatelse	60 days	Mon 23.01.23	Fri 14.04.23	[Task bar]											
3		Kontrahering	47 days	Thu 18.05.23	Fri 18.08.23	[Summary bar]											
4		Utsendelse anbudsgrunnlag	0 days	Thu 18.05.23	Thu 18.05.23	[Milestone 18.05]											
5		Anbudsregning tilbydere	20 days	Fri 19.05.23	Thu 15.06.23	[Task bar]											
6		Evaluering tilbud	5 days	Fri 16.06.23	Thu 22.06.23	[Task bar]											
7		Tilbudsavklaringer og forhandlinger	5 days	Fri 23.06.23	Thu 29.06.23	[Task bar]											
8		karenstid	10 days	Fri 30.06.23	Thu 10.08.23	[Task bar]											
9		Kontrahering	5 days	Mon 14.08.23	Fri 18.08.23	[Task bar]											
10		Totalentreprise inkl. Detaljprosjektering	200 days	Mon 21.08.23	Fri 31.05.24	[Summary bar]											
11		mobilisering	10 days	Mon 21.08.23	Fri 01.09.23	[Task bar]											
12		Detaljprosjektering	60 days	Mon 04.09.23	Fri 24.11.23	[Task bar]											
13		Utførelse	130 days	Fri 24.11.23	Fri 31.05.24	[Summary bar]											
14		Oppstart	0 days	Fri 24.11.23	Fri 24.11.23	[Milestone 24.11]											
15		Graving tekniske føringer	15 days	Mon 27.11.23	Fri 15.12.23	[Task bar]											
16		Klargjøring av lomp I Løvstakklien 11	5 days	Mon 27.11.23	Fri 01.12.23	[Task bar]											
17		Riving og rehab - Løvstakklien 34 B	40 days	Mon 04.12.23	Fri 02.02.24	[Task bar]											
18		overlevering 34 B	0 days	Fri 02.02.24	Fri 02.02.24	[Milestone 02.02]											
19		Riving og rehab - Løvstakklien 34 D	40 days	Mon 05.02.24	Fri 29.03.24	[Task bar]											
20		Overlevering Løvstakklien 34 D	0 days	Fri 29.03.24	Fri 29.03.24	[Milestone 29.03]											
21		Riving og rehab - Løvstakklien 34 C	40 days	Mon 01.04.24	Fri 24.05.24	[Task bar]											
22		overlevering Løvstakklien 34 C	0 days	Fri 24.05.24	Fri 24.05.24	[Milestone 24.05]											
23		Nedrigg	5 days	Mon 27.05.24	Fri 31.05.24	[Task bar]											

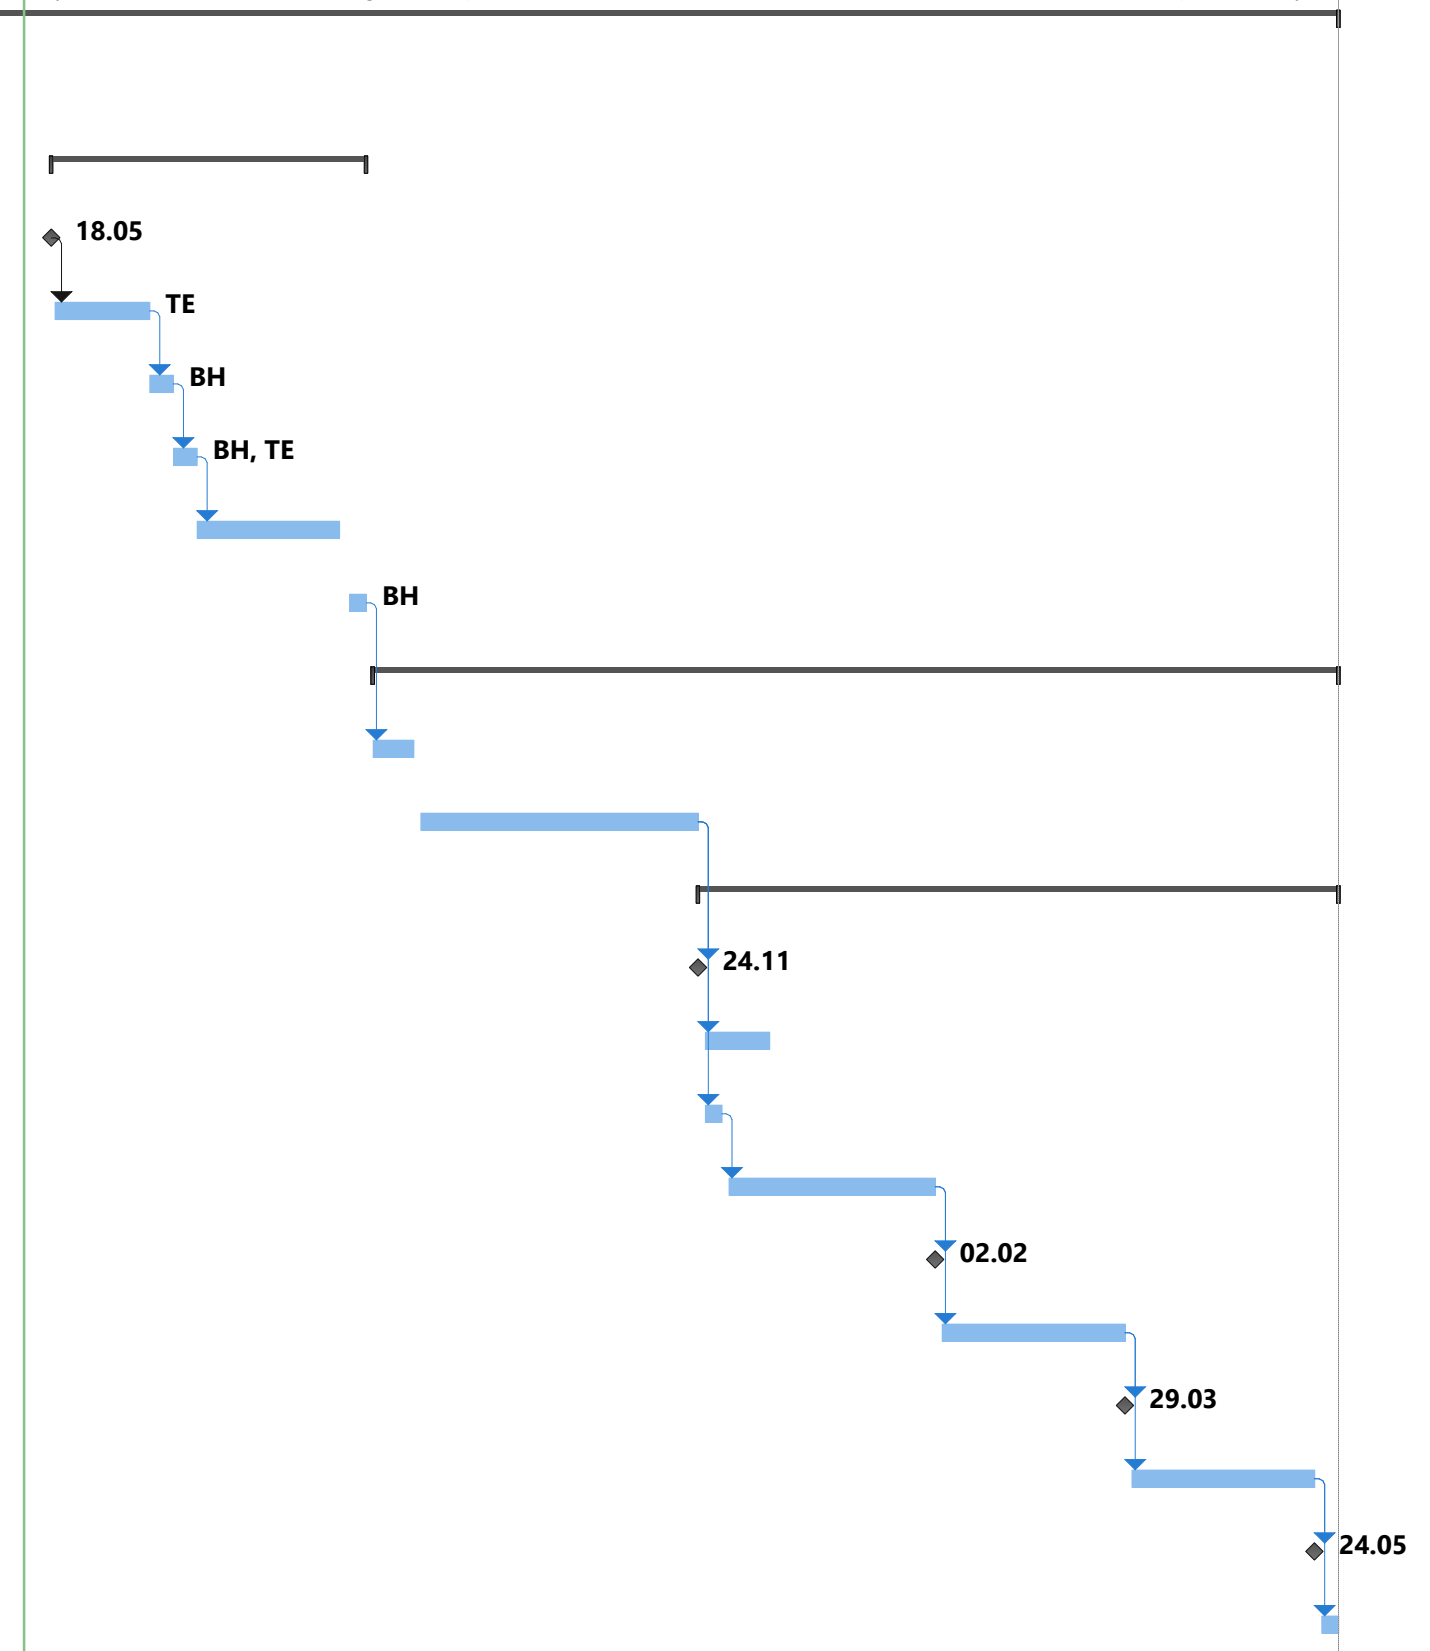

Project: 210304 Tentativ fremdriftsplan Date: Wed 10.05.23	Task		Project Summary		Manual Task		Start-only		Manual Progress		Deadline
	Split		Inactive Task		Duration-only		Finish-only		Manual Progress		Progress
	Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress		Manual Progress
	Summary		Inactive Summary		Manual Summary		External Milestone		Manual Progress		Manual Progress
